BUREAU OF RECLAMATION

Navajo-Gallup Water Supply Project (NGWSP)

Turnout Buildings Pre-Bid Conference Site Tour

August 26, 2026


Agenda

- Introduction
- NGWSP Overview
- Turnout Building Locations and Scope
- Procurement Requirements
- Travel Plan
- JHA
- Questions
- Adjourn

NGWSP Background


- Description
  - Currently estimated at $2.4 Billion
  - 2 Main Laterals (Cutter and San Juan) totaling 300 miles of Pipelines (20”-48”)
  - 2 Conventional Water Treatment Plants with ultimate capacity of 5 & 38 MGD
  - 19 Pumping Plants -- raw and finished water
  - 13 Turnout Buildings
  - Numerous Storage Tanks
  - Construction began in June 2012
  - Scheduled to end in December 2028

Project Overview Map

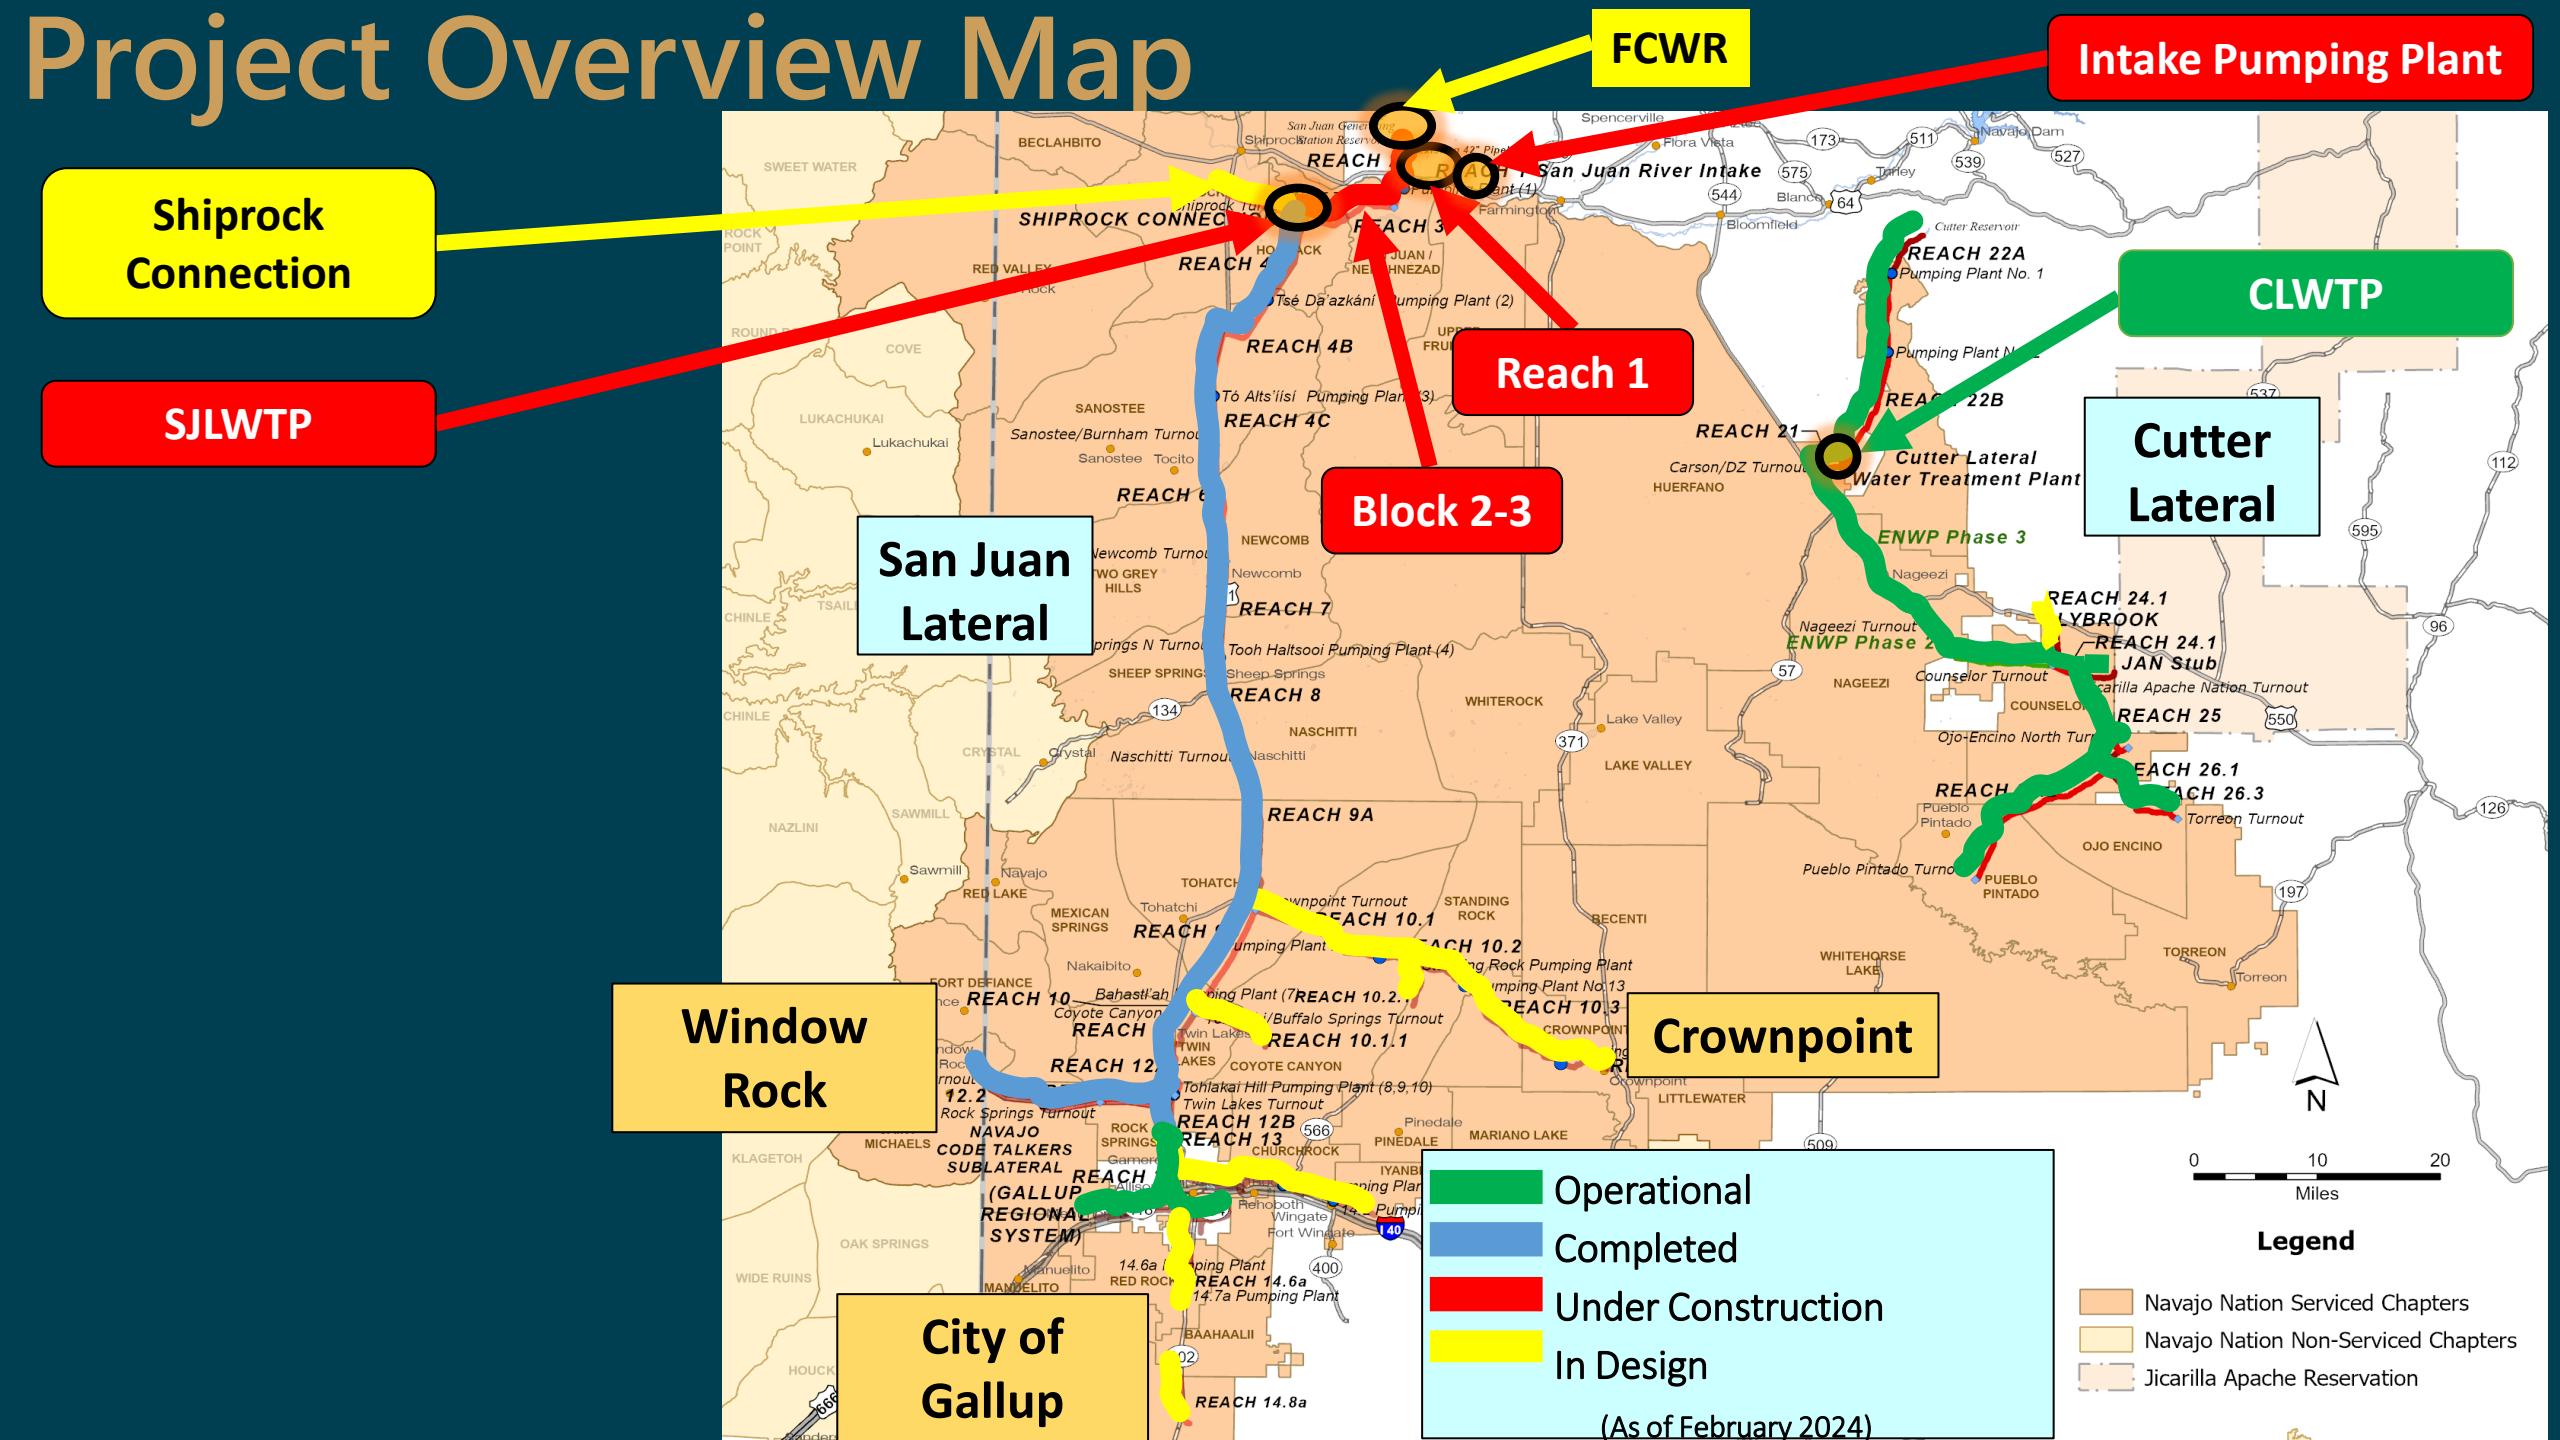

Turnout Building Locations

Item #	Reach #	Turnout Building Name
1	4C	Sanostee
2	6	Newcomb
3	8	Naschitti
4	9	Crownpoint (BBN9 R10.1)
5	10	Coyote Canyon
6	12.1	Rock Springs
7	12.2	Window Rock

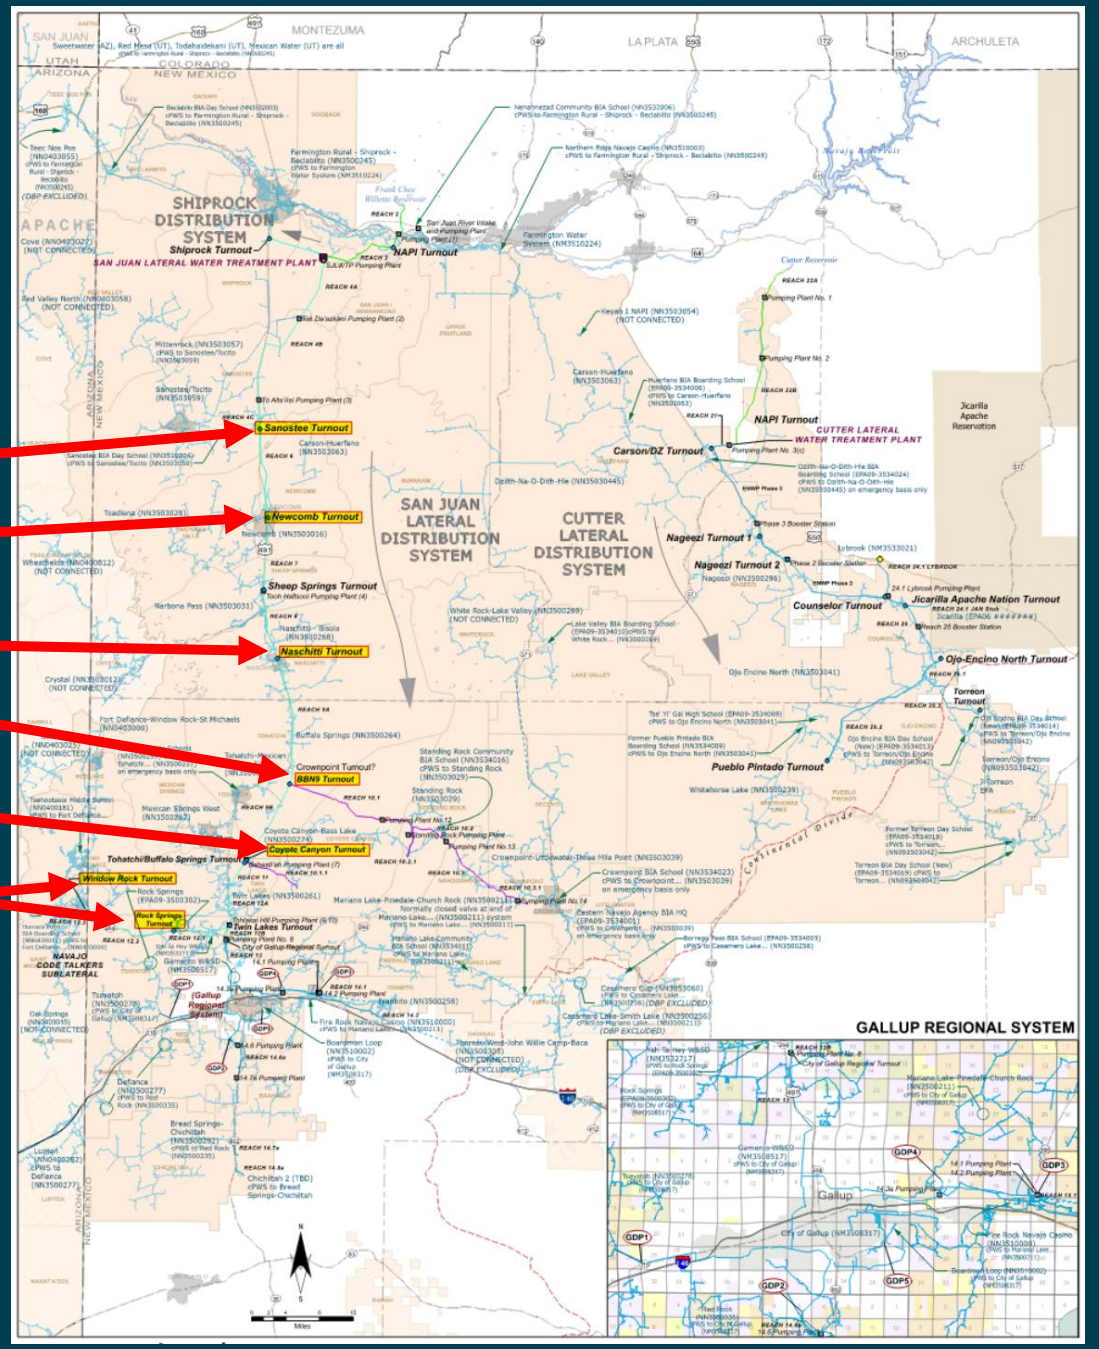


Turnout Building Scope

- **Precast concrete building**
  - ❖ Contractor design, including building, floor slab and foundation
  - ❖ Building mechanical, electrical, controls and security
- **Pipe and valving**
  - ❖ Connection to lateral distribution pipe (supply)
  - ❖ Connection to cPWS distribution pipe (delivery)
  - ❖ Interior exposed piping, valves, and accessories
  - ❖ Buried piping, valves, and accessories
- **Sitework**
  - ❖ Fenced site with gate
  - ❖ Buried thrust blocks
  - ❖ Gravel surfacing
  - ❖ Drainage
  - ❖ Access Roads
    - Coyote Canyon and Window Rock only
    - Low water crossing at BBN9
- **Controls integration with existing San Jaun Lateral SCADA System**
- **Fiber optic cable infrastructure**
- **Project Power**
  - ❖ Transformer provided by NTUA


Turnout Features


- Connection to lateral distribution pipe (supply)
- Upstream turnout isolation valve
- Connection to cPWS distribution pipe (delivery)
- Iron Fence with vehicle access gates
- Fiber and power location varies per site
- 80’ Permanent ROW

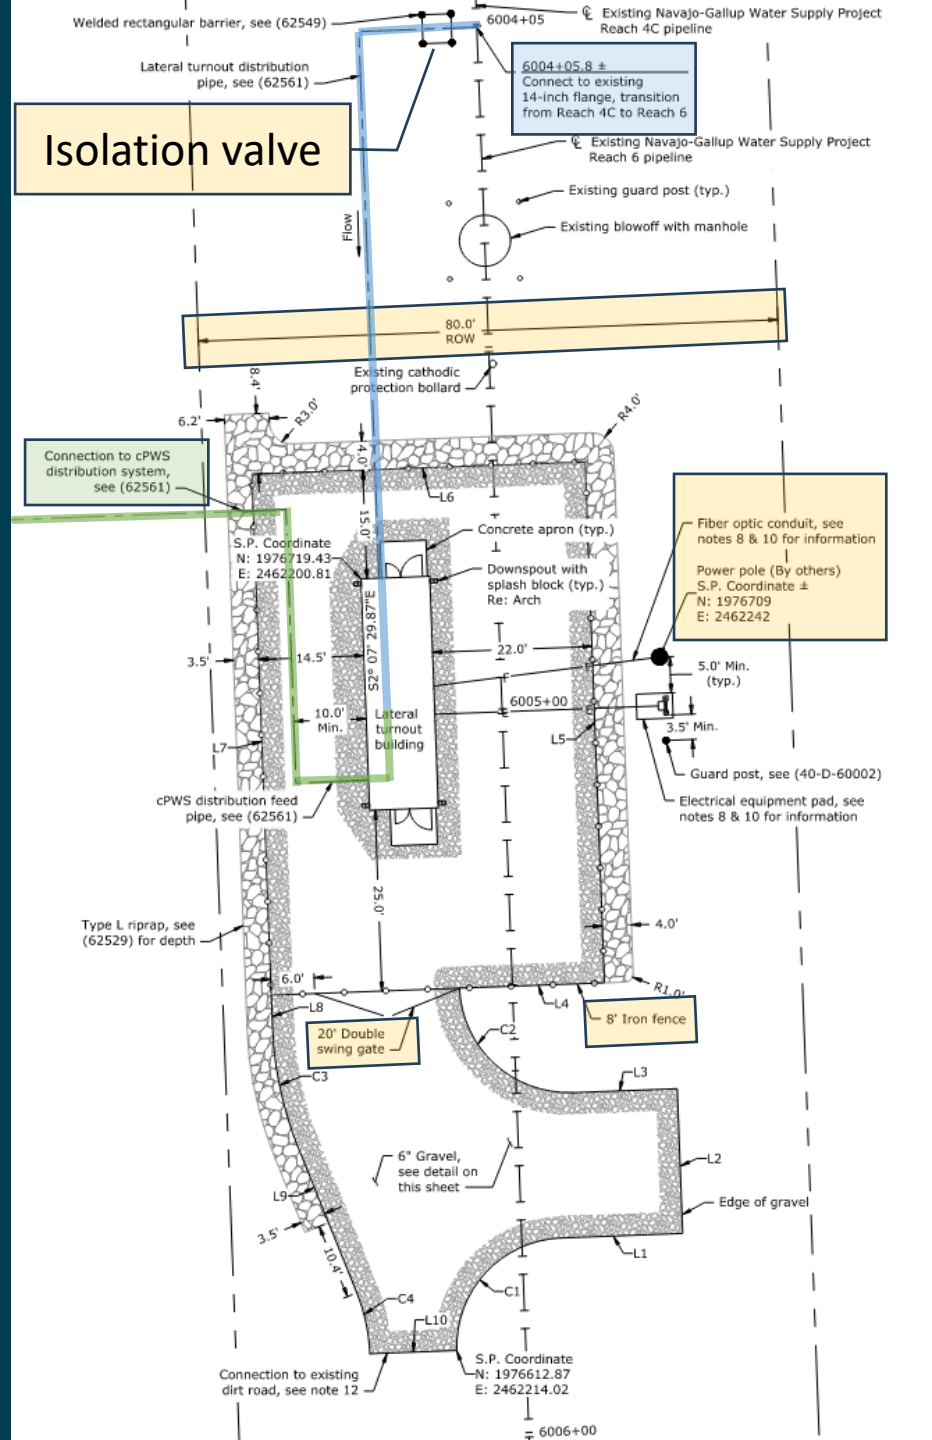

Turnout Building

- Standardized layout, with a few exceptions at Window Rock turnout
  - Precast concrete building footprint is larger
  - Larger dia. Pipe (12”)
  - No double check valve
  - No flow control valve

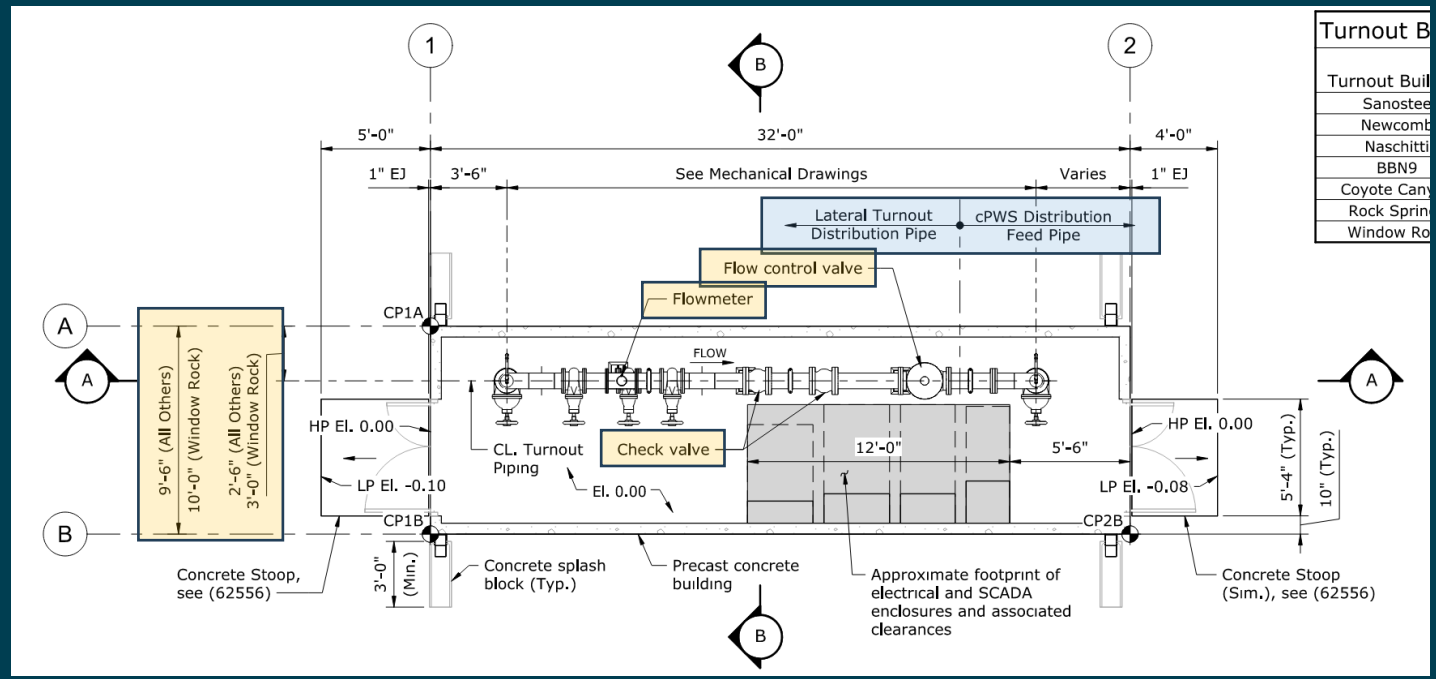

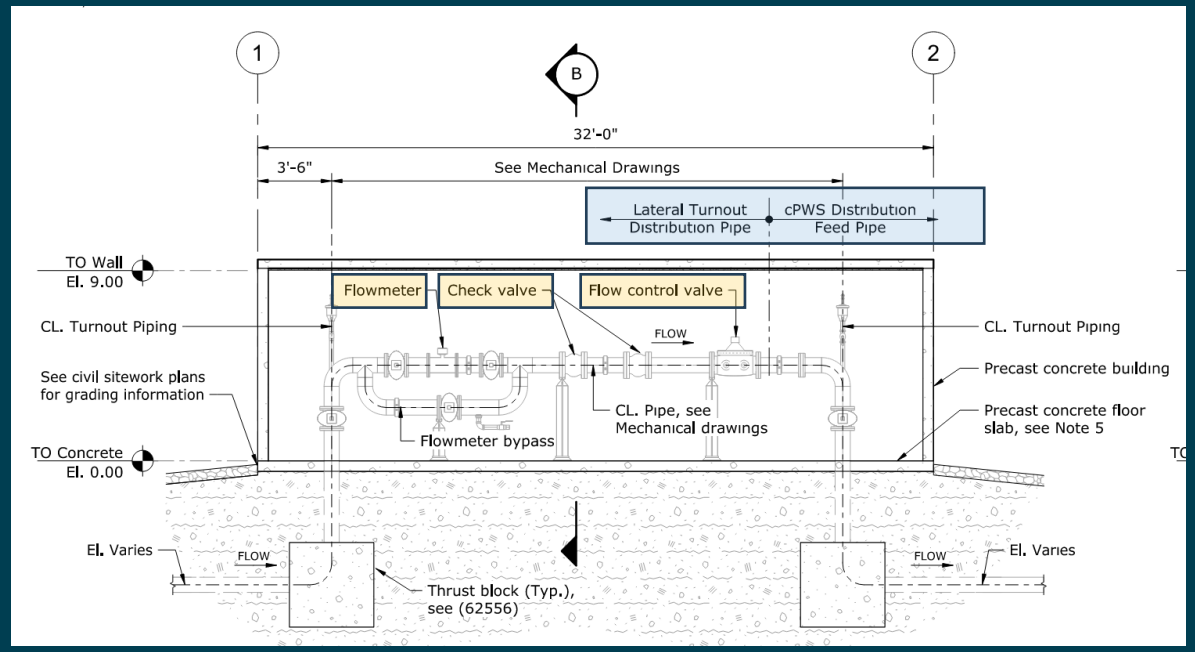







- Photo of interior exposed piping, valves and accessories at an existing turnout

Turnout Features – Site Specific

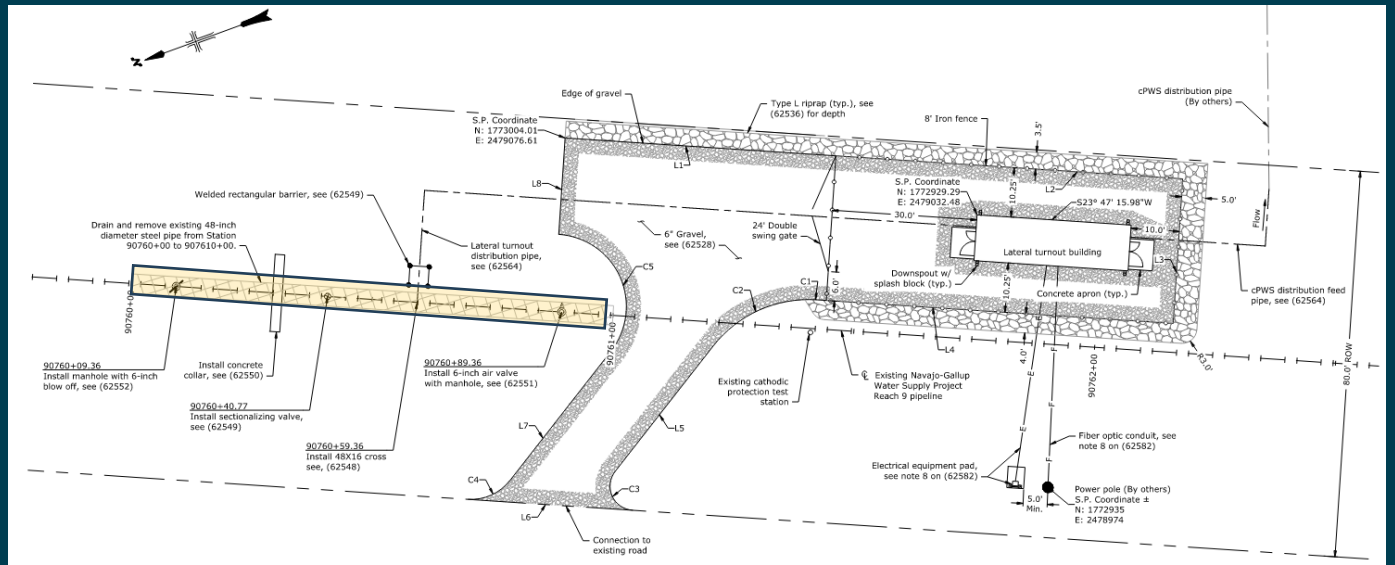

BBN9 Turnout

Connection to 48” diameter lateral distribution pipe to be constructed.

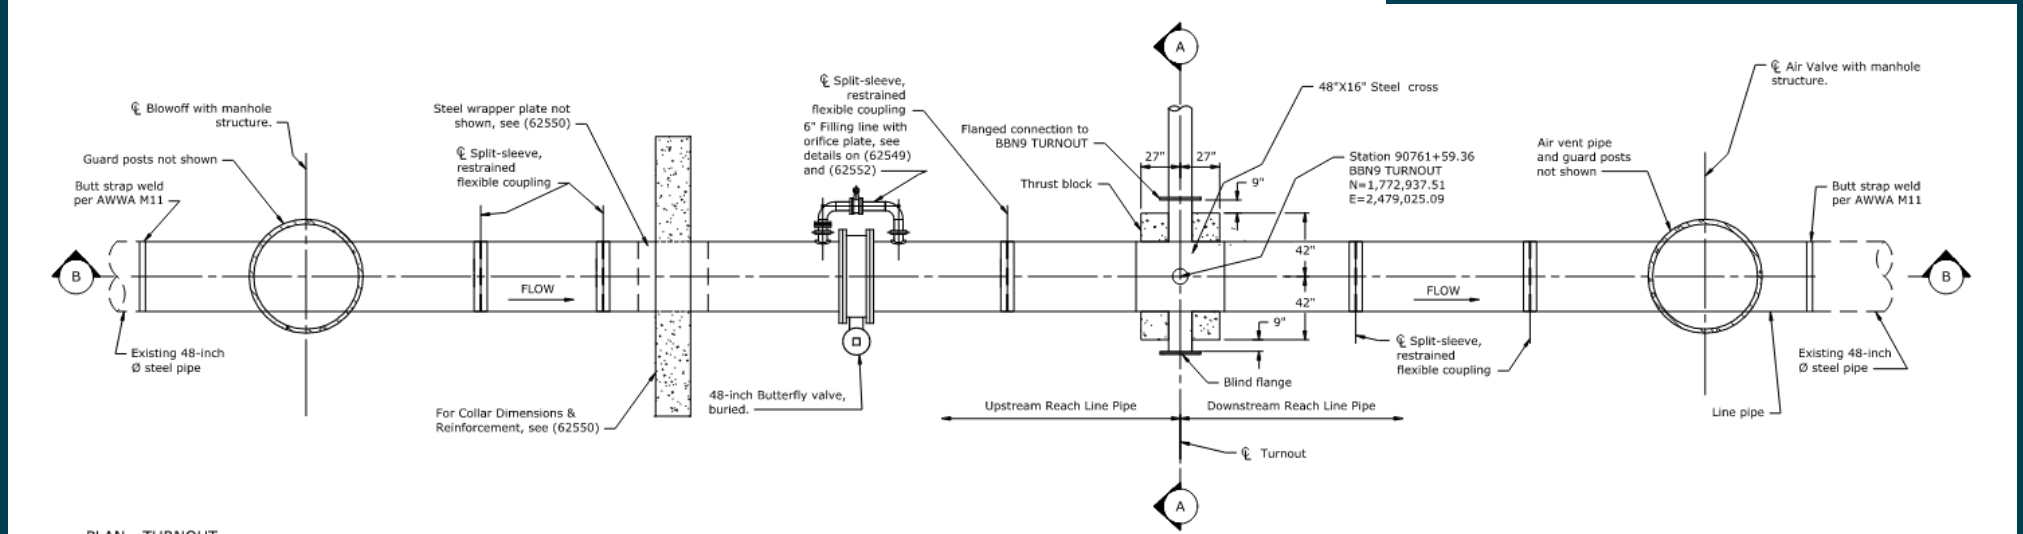


PLAN - TURNOUT

NOT TO SCALE - See (62535) for location

Turnout Features – Site Specific

Coyote Canyon Turnout

Connection to 42” diameter lateral distribution pipe to be made at existing sectionizing valve.

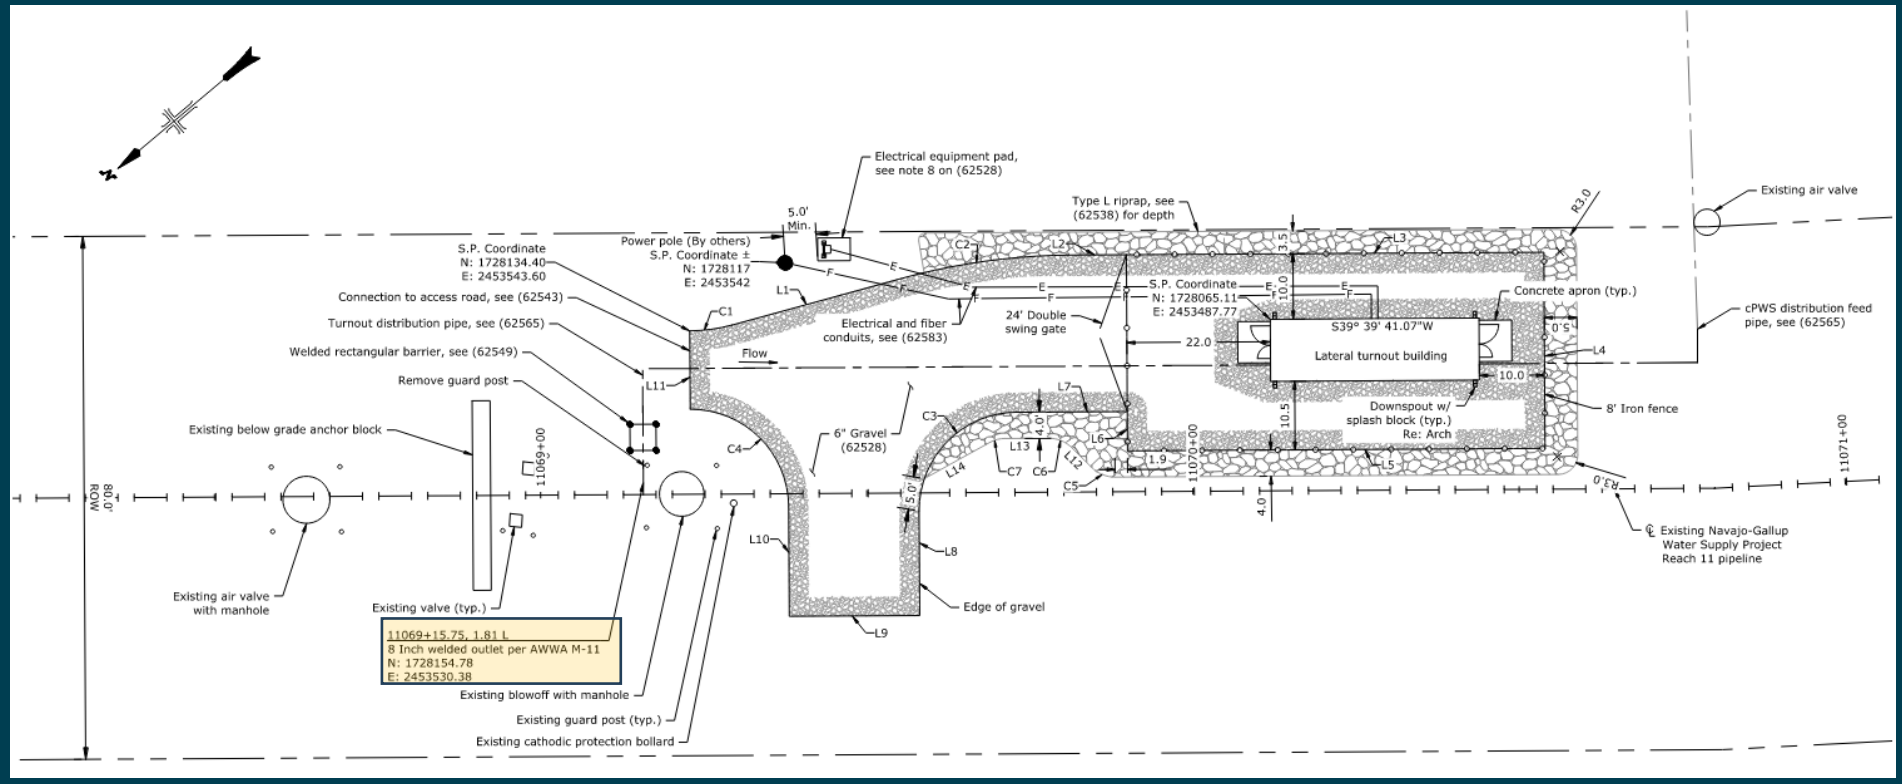

Turnout Buildings

Schedule & Hydraulic Requirements

6” Dia. Pipe
233 psi Max. Pressure
2.27 cfs Max. Flow

8” Dia. Pipe
184 psi Max. Pressure
1.52 cfs Max. Flow


6” Dia. Pipe
210 psi Max. Pressure
1.77 cfs Max. Flow

8” Dia. Pipe
123 psi Max. Pressure
3.80 cfs Max. Flow

6” Dia. Pipe
230 psi Max. Pressure
1.25 cfs Max. Flow

12” Dia. Pipe
138 psi Max. Pressure
11.51 cfs Max. Flow

6” Dia. Pipe
148 psi Max. Pressure
1.71 cfs Max. Flow

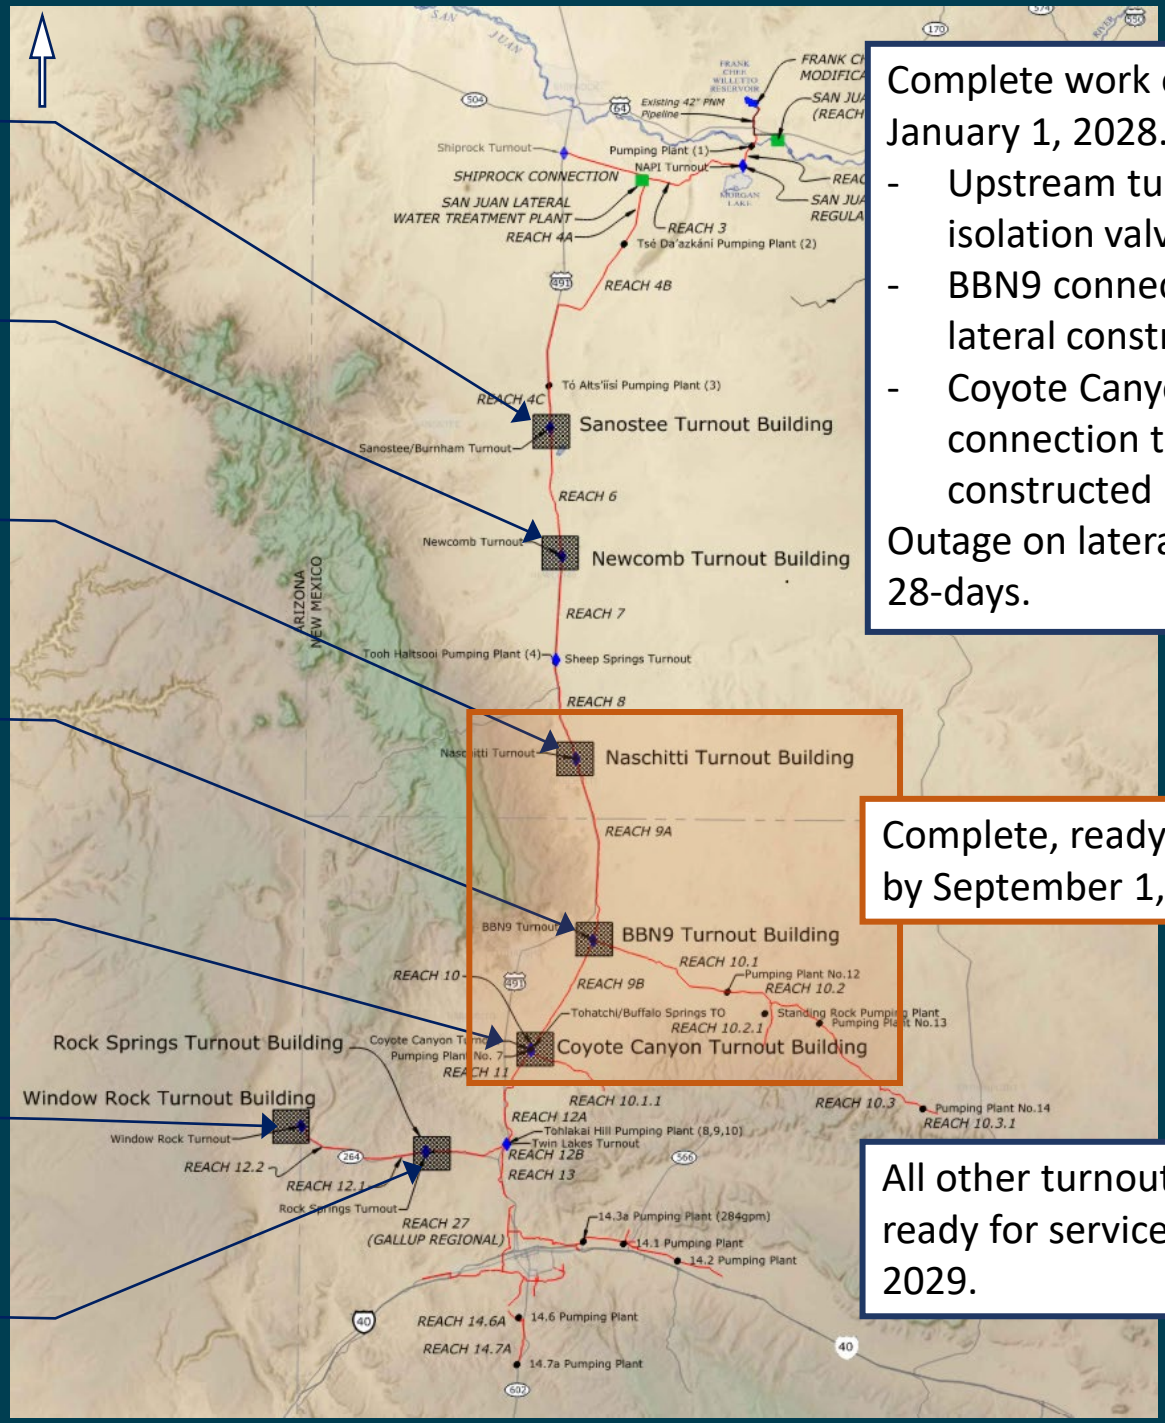

Complete work on lateral by January 1, 2028.

- Upstream turnout isolation valves
- BBN9 connection to lateral constructed
- Coyote Canyon connection to lateral constructed

Outage on lateral limited to 28-days.

Complete, ready for service, by September 1, 2028.

All other turnouts complete, ready for service, by April 1, 2029.

Travel Plan

1. Newcomb (36°17'18.40"N, 108°42'17.64"W)
2. BBN9 (Crownpoint) (35°52'11.04"N, 108°39'25.69"W)
3. Coyote Canyon (35°44'45.89"N, 108°44'30.37"W)
4. Window Rock (35°39'48.01"N, 109° 2'43.38"W) Turnout Buildings

Job Hazard Analysis



JOB HAZARD ANALYSIS

PROJECT: NGWSP Turnout Buildings **JOB HAZARD ANALYSIS No.-Rev.:** 1-0

OPERATION TO BE PERFORMED: Contractors Site Visit. Site visit Turnout Building Sites for Newcomb, BBN9 (Crownpoint), Coyote Canyon, and Window Rock

DATE: 08-26-2026

Note: SEE FOLLOWING PAGES FOR ADDITIONAL INFORMATION

Operation Sequence Number	Equipment or Crafts Required	Potential Hazards
01 – Travel to site	Government vehicle (GOV) and Personal Vehicle (POV)	Hazard Designation 1 (HD1): Flat tire, mechanical breakdown, traffic congestion, bad roads, road construction, refueling, unsafe drivers, icy road conditions. HD2: Working outdoors, sunburn, ritters, wild animals, weather, uneven ground, slips/trips/falls, water safety.
02 – Review hazards on site before beginning work and revise JHA as needed based on additional hazards identified or changes in work	GOV, PPE as needed	
03 -Walk around turnout building sites		
04 - return to office	GOV and POV	

Personnel Participating:	Certifications:	Training:
FCCO, TSC and Contractors	NA	NA

Job Hazard Analysis



SPECIFIC JOB HAZARD ANALYSIS PROCEDURES

Operation Sequence Number	Hazard Designation Number	Solution to Hazards	Personal Protective Equipment and Safety Equipment	Reference Safety Manual
General	**General**	ALL non-Reclamation Visitors must be escorted to the field by project personnel familiar with the site and conditions. FCCO will provide a brief description of activities and site orientation for visitors. Close gate when leaving site.		2 (Medical Services and First Aid)
01	**HD1**	Park vehicles out of the way of construction or other work being performed on site and keep away from construction zones in a safe location. Follow instructions from project personnel. Drive defensively always use caution (there maybe icy road conditions). Inform supervisor of route and expected timing of site visit start and end. Confirm cellular service is available at the site location.	GOV and POV in safe operating condition, cell phone with service.	11.7.5 (Refueling) 29 (Driving)
02	**HD2**	Apply sun protection, hydrate as needed, confirm proper PPE is being worn for task, do not work alone. Watch footing (uneven ground) to prevent trips, don't walk in tall vegetation as snakes could be present, if working around river without handrails. Be prepared for weather conditions and changes, by wearing appropriate clothing. When lightning is 5 miles away, get in vehicle (FCCO staff will monitor).	Jacket/pants/gloves, sun protection, closed footwear suitable for field work, have a cell phone with service, (if applicable hard toe boots, safety vest, gloves, safety glasses, hard hat required in construction sites).	7 (Health Hazard Assessment) 13 (Walking and Working Surfaces)

Job Hazard Analysis



EMERGENCY RESPONSE PROCEDURES
In the event of emergency, assess safety of site/surroundings, and immediately call 911 **CDSR Contact(s):** Dalton Reese – (505) 386-6827; Hilda Castillo-Smith – (505) 239-4558 **Supervisor:** Moncef Tihami – (505) 386-6751 **Nearest Hospitals (Google Maps link in QR code):** San Juan Regional Medical Center 801 W Maple St, Farmington, NM 87401 Rehoboth Mckinley Christian Health Care Services 1901 Redrock Dr, Gallup, NM 87301 - (505)863-7136


BUREAU OF
RECLAMATION
